

**NOVELLE SAN JOSE
FRAMING ACTIVITIES
MONDAY 2/26/2024**

SCHEDULE COVERAGE & DESCRIPTION

PAGE #1 Exterior Envelope

PAGE #2 Roof Framing

PAGE #3 Long Lead Items

**COORDINATION MEETINGS HELD EVERY MONDAY
@ 10:00AM**

**ATTENDANCE IS MANDATORY FOR THOSE
WHO APPEAR ANYWHERE ON THIS
SCHEDULE.**

**MEETING HELD IN THE CONSTRUCTION OFFICE
LOCATED @ 3355 ALMADEN EXPRESSWAY S.J C.A**

LEGEND:

	= WORK THAT HAS BEEN COMPLETED
	= WORK THAT IS TO BE PERFORMED
B	= WORK THAT IS BEHIND SCHEDULE
C	= SCHEDULED CONCRETE POUR
D	= SCHEDULED DELIVERY
I	= SCHEDULED INSPECTION
M	= WORK MUST BE COMPLETE BY
W	= WEATHER DELAY

FRAMING ACTIVITIES

PREPARED BY: John Perino
Monday, March 4, 2024

DESCRIPTION	FEBRUARY							MARCH														April																										
	Last Week			This Week				2nd WEEK				3rd WEEK				4th WEEK				5th WEEK			6th WEEK																									
	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S		M	T	W	T	F	S	S	M	T	W	T	F	S	S					
	26	27	28	29	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24		25	26	27	28	29	30	31	1	2	3	4	5	6	7	8	9	10	11	12
1	Exterior Envelope																																															
2	Zone																																															
3	First floor thresholds																																			SID CEBALLOS												
4	Knife Plate brackets																																			SKYLINE SYSTEMS												
5	Remaining DensGlass																																			ADCO												
6	Hot Rubber																																			KODIAK												
7	Remaining Window install																																			LIGHTHOUSE												
8	SAM in Soffits																																			KENYON												
9	Any Remaining Ext. Penetrations																																			ALL MEPS												
10	Level 4 B - 11 Envelope																																															
11	First floor thresholds																																			SID CEBALLOS												
12	Knife Plate brackets																																			SKYLINE SYSTEMS												
13	Remaining DensGlass																																			ADCO												
14	Hot Rubber																																			KODIAK												
15	Remaining Window install																																			LIGHTHOUSE												
16	SAM in Soffits																																			KENYON												
17	Any Remaining Ext. Penetrations																																			ALL MEPS												
18	Level 4 C - 18 Envelope																																															
19	First floor thresholds																																			SID CEBALLOS												
20	Knife Plate brackets																																			SKYLINE SYSTEMS												
21	Remaining DensGlass																																			ADCO												
22	Hot Rubber																																			KODIAK												
23	Remaining Window install																																			LIGHTHOUSE												
24	SAM in Soffits																																			KENYON												
25	Any Remaining Ext. Penetrations																																			ALL MEPS												
26	*Level 4 D - 9 Units Framing																																															
27	Layout 3 Days																																			ADCO												
28	Stand LB Walls 6 Days																																			ADCO												
29	CRC & Backing 5 Days																																			ADCO												
30	Shear 5 Days																																			ADCO												
31	Instal HSS 1 Day																																			ADCO & BERGER												
32	Rim Track & Joists 6 Days																																			ADCO												
33	Decking 8 Days																																			ADCO												
34	Deck Screw inspection 1Day																																			CITY OF SJ												
35	Parapets																																			ADCO												

FRAMING ACTIVITIES

PREPARED BY: John Perino
Monday, March 4, 2024

DESCRIPTION	FEBRUARY							MARCH														April																										
	Last Week			This Week				2nd WEEK				3rd WEEK				4th WEEK				5th WEEK				6th WEEK																								
	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S		M	T	W	T	F	S	S					
	26	27	28	29	1	2	3	4	5	6	7	8	9	10	11	12	13	14	15	16	17	18	19	20	21	22	23	24	25	26	27	28	29	30	31		1	2	3	4	5	6	7	8	9	10	11	12
78	Layout walls																																			ADCO & REACO												
79	Build mechanical platforms																																			ADCO												
80	Install Roof Anchor																																			SAFE GUARD												
81	Plumbing penetrations																																			CJS												
82	Stand pipe																																			AFS												
83	Mech Penetrations																																			REACO												
84	Elec Penetrations																																			JMB												
85	Insulate Parapets																																			TRI COUNTY												
86	City Inspection																																			CITY OF SJ												
87	Densdeck Parapets																																			ADCO												
88	Roof material delivery																																			KODIAK												
89	Roof installation																																			KODIAK												
90	Long Lead Items																																															
91	Overhead Roll up Door 12-10-2024																																															
92	Smoke Curtain 4-1-24																																															
93	Elevator 7-6-2024																																															
94	Cabinet Del																																															
95	Switch Gear Bus Duct Feb Pad /March 2024																																															
96	Gypcrete Start March 2024																																															

NOVELLE SJ INTERIOR SCHEDULE MONDAY, 03/04/2024

SCHEDULE COVERAGE & DESCRIPTION


PAGE #1 L4 ZONE A

PAGE #2 L3 ZONE A

PAGE #3 L2 ZONE A

PAGE #4 ACTIVITIES OUT OF SEQUENCE

PAGE #4 L4 ZONE B

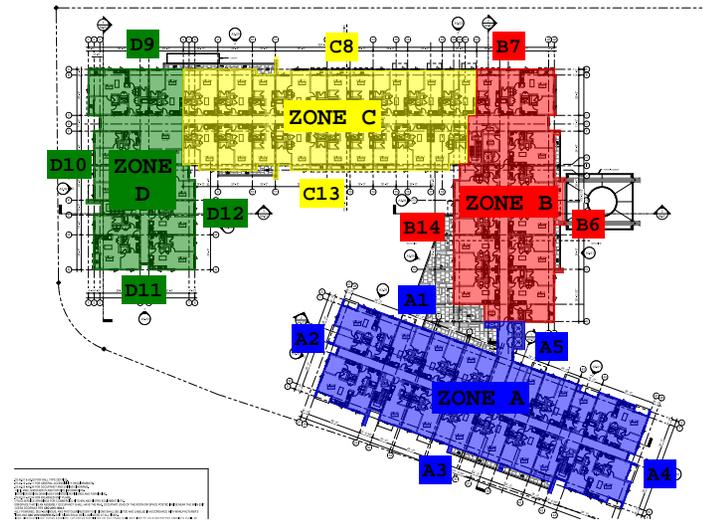

LEGEND:

-  = WORK THAT HAS BEEN COMPLETED
-  = WORK THAT IS TO BE PERFORMED
-  = WORK THAT IS BEHIND SCHEDULE
-  = SCHEDULED CONCRETE POUR
-  = SCHEDULED DELIVERY
-  = SCHEDULED INSPECTION
-  = WORK MUST BE COMPLETE BY
-  = WEATHER DELAY

**COORDINATION MEETINGS HELD EVERY MONDAY
@ 10:00AM**

**ATTENDANCE IS MANDATORY FOR THOSE
WHO APPEAR ANYWHERE ON THIS
SCHEDULE.**

**MEETING HELD IN THE CONSTRUCTION OFFICE
LOCATED @ 3355 ALMADEN EXPRESSWAY SJ CA.**

